



## Construction Newsletter No. 17

March 18, 2016

### On-Going

Here's a block-by-block breakdown of the work currently underway:

- **Lees Avenue to Hazel Street:** Gas main installation.
- **Clegg Street to the Rideau River:** Camera inspection of the sewers.
- **Rideau River Drive:** Sanitary sewer installation.

### Upcoming

Here are key **new** upcoming construction activities planned for the next two weeks:

- **Clegg Street to Riverdale Avenue:** Hydro Ottawa will remove their cables from the old concrete poles and Bell Canada will transfer their cable from the old concrete poles to the new wood poles.



*Gas main installation on west side of Main Street.*

### Traffic

#### Rideau River Drive

**Rideau River Drive is closed to traffic at the cul-de-sac (approximately 130m south of Main Street).** During that period, Rideau River Drive is converted to a two-way street between Main Street and the cul-de-sac. On-street parking is also removed.

#### Colonel By Drive


The St. Patrick's Day Run will take place on Saturday March 19<sup>th</sup>. For this event, **Colonel By Drive will be closed to traffic from Hog's Back Road to Hawthorne Avenue from 7:30 a.m. to 11 a.m.**



# Main Street Renewal

## Did you know?

Utility poles are often shared by multiple utility companies. The poles belong to one utility company and agreements are in place for others to occupy the poles. For safety purposes, Hydro cables will always be at the top of the poles and telecommunication cables are the lowest. In the Ottawa area, the top wires on the hydro pole typically carry anywhere from 4,000V to 44,000V and the lower cables typically carry the household voltages; either 240V or 600V (depending on whether single phase or three phase power is required).

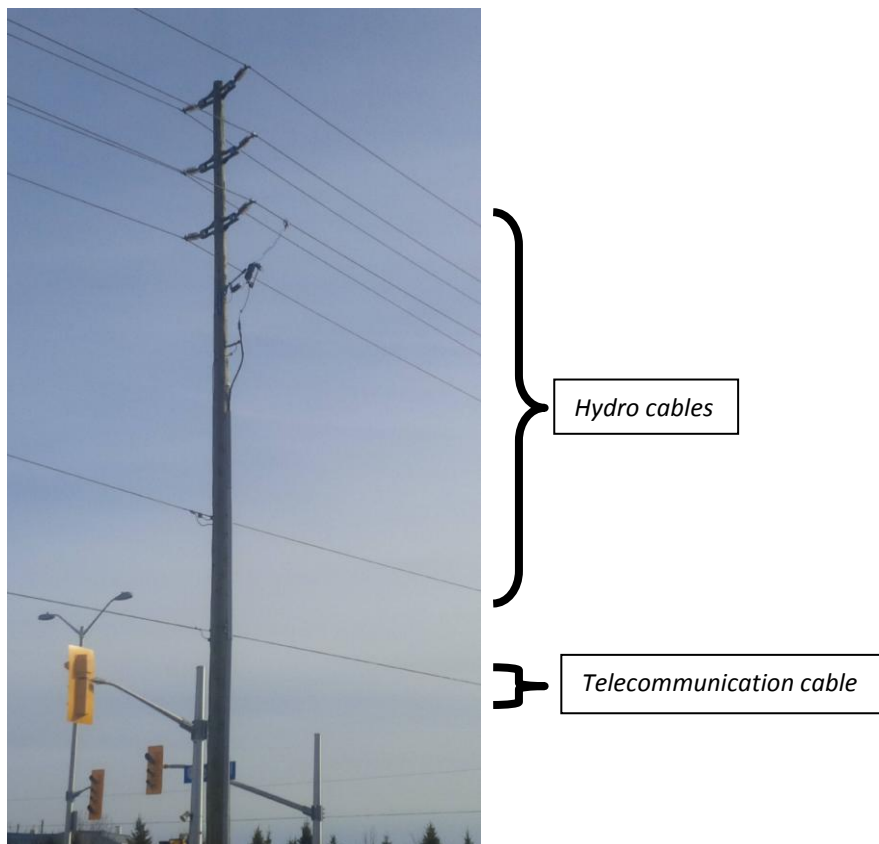

Accessible formats and communication supports are available, upon request, at the following link:  
[www.ottawa.ca/accessibleformat](http://www.ottawa.ca/accessibleformat)
